

Lawrence Public Library Milestone Schedule

Updated 09.25.2012

September 2012

- 20 HRC approval of exterior modifications
2nd public meeting for parking garage extra level tax benefit district
- 25 City Commission to consider resolution for parking garage extra level
Anticipate decision by end of October. BA Green to hold bids for 60 days.

October 2012

- 01 Borders lease begins. Borders construction remodel work to begin in October.
- 02 City Commission meeting – Approval of site plan submittal; authorize bidding
- 03 Garage and Site Package out for printing and bidding
- 05 % for Art - RFQ and sketch submissions due
- 23 Issue last addendum for Garage and Site Package
- 30 Receive bids for Parking Garage and Site Package; public bid opening
- 31 Bid tab memo and recommendation to city manager
% for Art – finalists selected (finalist presentations and artist selection – Late 2012)

November 2012

- 06 City Commission meeting – approval of bids for Garage and Site Package
- 07 GMP signed by city manager
- 13 Issue Notice to Proceed for Garage and Site construction
- 15 Begin installation of electrical conduits and pull wire along Kentucky St right-of-way for new transformer to be located behind Fire Station and Senior Center. Work to continue through the end of November.
- 22 Thanksgiving
- 28 Electrical service changeover for Fire Station and Senior Center.
(Tentative date – expected late November or early December)

December 2012

- 03 City to remove parking meters from existing library lot
- 05 Close drive north of fire station and begin sanitary sewer work

Lawrence Public Library Milestone Schedule (cont'd.)

Updated 09.25.2012

December 2012 (cont'd.)

- 06 Close south half of existing library parking lot and Kentucky entrance. Keep 2 rows of parking spaces available at front of library and maintain Vermont entrance. Also, keep crosswalk open by Aquatic Center.
Library to begin moving into Borders.
- 09 Begin excavation for parking garage
- 17 Library soft opening at Borders. Existing library closed.
- 18 Re-open (temporary gravel) drive behind fire station
- 25 Christmas

January 2013

- 15 Issue Library Addition and Renovation Package for bid
- 29 Issue last addendum for Library Addition and Renovation package

February 2013

- 05 Receive bids for Library Addition and Renovation Package; public bid opening
- 12 City Commission meeting; approval of bids for Library Addition and Renovation package
- 13 GMP signed by city manager
- 19 Issue Notice to Proceed for Library Addition and Renovation construction
- 21 Start Library Addition and Renovation construction


June 2013

Parking garage construction complete

April 2014

Project construction complete. Library reopens.

All dates are indicated for planning purposes and subject to change.

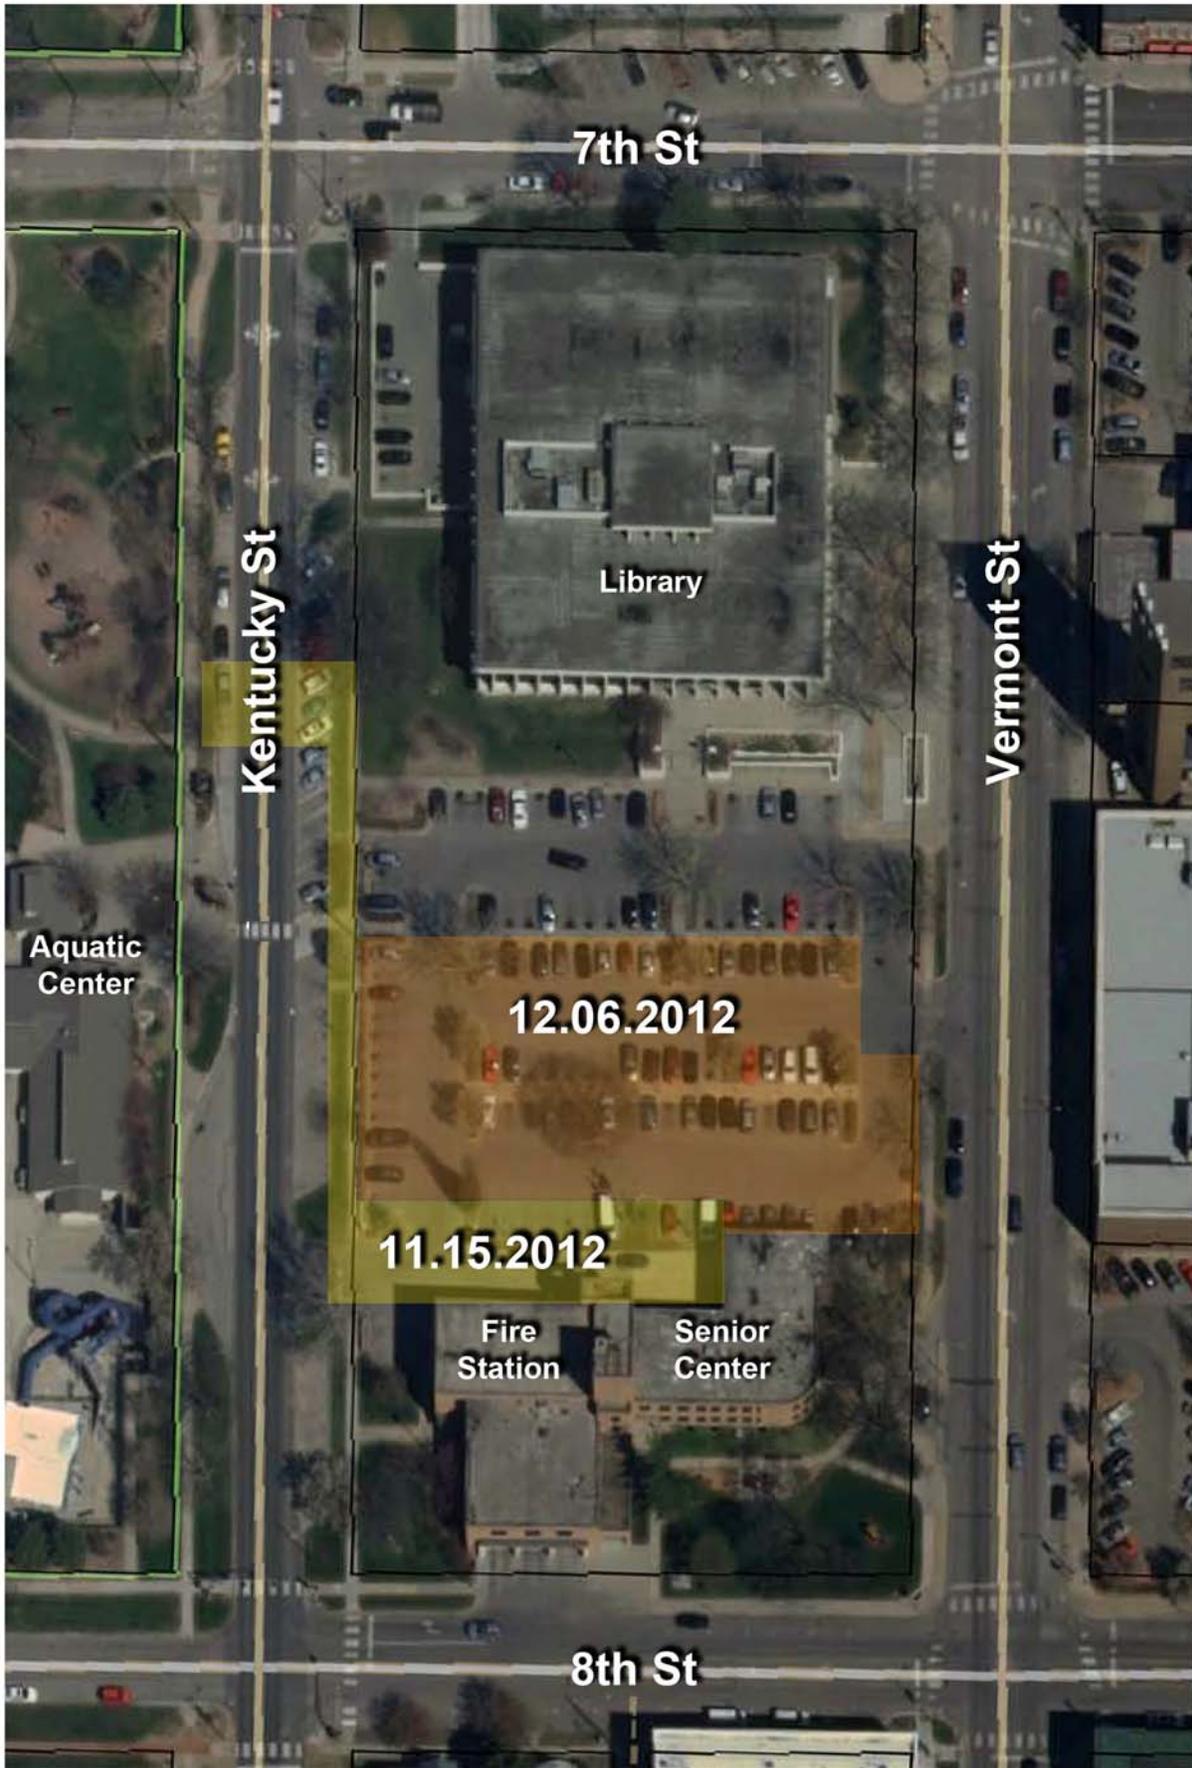

Refer to attached schedule for description of work associated with these dates.
