



**TRANSPORTATION COMMISSION
STUDY SESSION**


**Wednesday, September 19, 2018 3:30 PM
City Commission Room, City Hall, 6 E. 6th Street**

STUDY SESSION AGENDA

Public comment related to work session topics will be allowed at the end of each discussion item. Each person will be limited to three (3) minutes. Individuals are asked to come to the microphone, sign in, and state their name and address.

1. 2018 CIP Update and 2019 CIP Overview

Staff will provide an update on the 2018 CIP projects and provide an overview of the 2019 CIP projects that are relevant to Transportation Commission



2018 CIP Update and 2019 CIP Overview

Transportation Commission Study Session
September 19, 2018



2018 Project Update

- PW18E10CIP 23rd St Center Turn Lane – Mass to Louisiana
- PW18E10 Massachusetts St – 11th to 14th
- CI09 Sidewalk/Bike/Ped Improvement/ADA ramps
- CDBG ADA ramps and Haskell RRFB
- PW17E66CIP E 9th St Improvements
- PW18E7CIP 19th St – Iowa to Naismith




23rd Street Center turn Lane - Massachusetts to Louisiana

- Construction will begin in October 2018.
 - Phase 1 & 2 will be completed this fall to mill and overlay of 23rd Street between just east of Iowa Street to the west approach of Louisiana Street.
 - Phase 3 & 4 will begin in October but has a completion date of in Spring 2019. This work includes the widening of 23rd Street between Louisiana Street and Massachusetts Street as well as the installation of sidewalk on both sides, installation of new waterline from Louisiana Street to Barker Avenue, and the mill and overlay of 23rd Street from Louisiana Street to the Haskell Bridge.



Massachusetts Street Lane Realignment – 11th to 14th

- Project was bid in Aug 2018 but came in over budget.
- Mill and overlay was completed Aug 31, 2018 under the Pavement Maintenance contract. The contractor also installed the center lane markings.
- Project plans were updated and are out to bid. Bids will be opened on Sep 18, 2018.
- Project award scheduled for the Oct 2, 2018 City Commission meeting.
- Once a Notice to Proceed is issued the contractor has 20 working days to complete the project.



Sidewalk/Bike/Ped Improvements and CDBG Projects

Sidewalks and ADA Ramps

- CFS Engineers is currently working on plans for the projects.
- CDBG ramps and RRFB at 16th and Haskell will be bid as one project and the City funded ramps and sidewalks will be bid as one project.
- Project will be bid this winter and should be complete by spring or early summer.

Bicycle Boulevards

- Staff has selected a consultant and is working with them on a scope and fee. Targeting contract approval from City Commission on Oct 16, 2018.
- Will work with consultant on schedule for the project to target public meeting dates and a date to bring the conceptual design to Transportation Commission.



E. 9th Street Improvements

- New Hampshire to Pennsylvania (& Sidewalk to Delaware)
- Pavers, Inc. (Salina, KS) Low Bid: \$2,079,114.30
- Currently Closed from Connecticut to New Hampshire
- Work Began July 2018; Substantial Completion this winter. Bricks being salvaged and stored at 18th & Wakarusa




19th Street – Iowa to Naismith & Bike/ped tunnels

- Project Letting is in October
- Construction will begin in early 2019 with roadway impacts beginning Spring Break
- Phase 1 – Reconstruct 19th from Iowa to Ousdahl and install east half of Iowa tunnel.
- Phase 2 – Reconstruct 19th Street from Ousdahl to Naismith and complete west half of Iowa tunnel.



2019 CIP Projects

- CI09 Sidewalk/Bike/Ped Improvements/ADA Ramps
- CDBG funded projects
- PW18E2CIP Kasold – Clinton Parkway to 22nd St
- PW19E2CIP 6th and Tennessee Right Turn Lane
- PW17E3CIP E. 19th St – Harper to O'Connell
- PW17E10 Queens Road – 6th St to City Limits
- PR2121 CIP Lawrence Loop – Downtown Section



Sidewalk/Bike/Ped Improvements and CDBG Projects

Sidewalk/Bike/Ped Improvements


- Plan on discussing the next years projects in November with the Transportation Commission
- If we are awarded a TA grant the design funds and potentially the matching funds will have to come out of the 2019 local funds

CDBG

- \$303,035 of money for pedestrian projects
- A draft list of locations was approved by Transportation Commission in April
- A final recommendation on locations will be presented to Transportation Commission in November

Kasold- Clinton Parkway to 22nd

- \$1M in 2019 CIP
- Conceptual Plan
 - Shared-use path on the west side
 - Dual Turn Lanes at Clinton
 - Large "Cut" needed on east side to accommodate sidewalk improvements

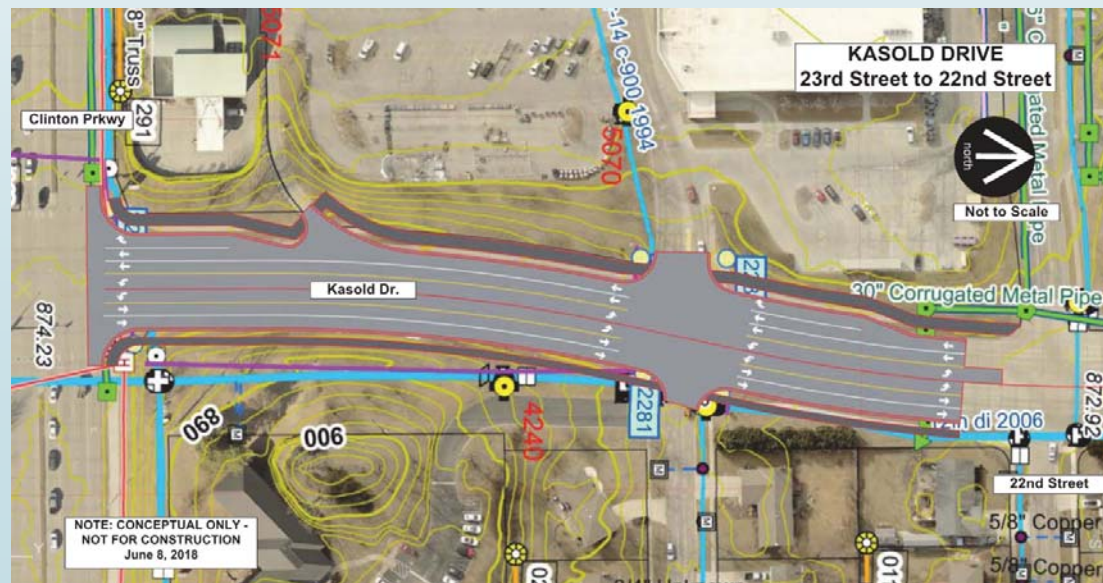



6th and Tennessee Right Turn Lane

- Add Right Turn Lane on EB 6th Street
- Add “bulb-out” to reduce pedestrian crossing distance on S. Leg of Tennessee
- Address Drainage Issues on S. Leg of Ohio
- Coordination w/ Historic Resources District
- Field Check Late Sept./Early Oct.
- Letting July 2019; Construction Late Summer/Fall 2019
- 80% Match from KDOT up to \$250,000
- \$250,000 included in 2019 CIP for City Funds



Queens Road – 6th to Eisenhower Drive

- Pending the approval of the benefit district construction would begin in 2019.
- One lane NB; one lane SB; center turn lane/median
- Roundabout at Overland Drive
- Bike lanes and shared-use path
- Traffic Signal at 6th & Queens Road



E. 19th Street – Harper to O'Connell

- \$3.625M in 2019/2021 CIP
- Design will review multiple cross sections with varying bike/ped accommodations
- Possible roundabout at Harper
- Waterline reconstruction in 2019; street reconstruction in 2021



Lawrence Loop – Downtown Sections

- 2019 CIP includes \$100,000 for study/design of preferred alignment of Downtown segment of Lawrence Loop
