
ID	0	Task Name	4/22	May 4/29	5/6	5/13	5/20	June 7 6/3	6/10	6/17	6/24	July 7/1	7/8	7/15	7/22	Aug 7/29	8/5	8/12	8/19 8/2	Sep 26 9
1	1	1.0 Project Initiation, Coordination, and Management	!											i i				'	l P	
2		1.1 Kickoff (1)																		
3	1	1.2 T2030 Committee Meetings (Monthly)																		
4		T2030 Committee Meeting - 1																		
5		T2030 Committee Meeting - 2																		
6		T2030 Committee Meeting - 3																		
7		T2030 Committee Meeting - 4																		
8		T2030 Committee Meeting - 5																		
9		1.3 T2030 Teleconferences (Monthly)																		
10		T2030 Teleconference - 1																		
11		T2030 Teleconference - 2																		
12		T2030 Teleconference - 3																		
13		T2030 Teleconference - 4																		
14		T2030 Teleconference - 5																		
15	1	1.4 Lawrence/Douglas County MPO Meetings																		
16		MPO Meeting - 1						1												
17		MPO Meeting - 2																		
18		MPO Meeting - 3																		
19		1.5 Ad Hoc Meetings (3)										1								
20	-	1.6 Project Management/Administration										-								
21		Project Management/Administration										1								
22		Project Implementation Plan/Quality Assurance Plan																		
23		Project Schedule																		
24		Progress Reports/Invoices										1				l				
25		Document Control										1				:				
26																				
27		2.0 Public and Stakeholder Participation																		<u> </u>
28		2.1 Public and Stakeholder Participation Plan																		
29		2.2 Public Outreach - Getting the Word Out																		
30		Website										1				l				
31		Water Bill Inserts																		
32		Post-It Ads						 :				:								<u> </u>
33		Media Releases														:				
34		Flame Newsletter																		
35		Project Newsletter														:				<u> </u>
36		Transit Bus Ads																		
37		2.3 Public Meetings (3)																		
38		Public Meeting - 1																	•	
39		Public Meeting - 2																		
40																				
41		2.4 Stakeholder Meetings																		
42		Stakeholder Interviews (2 Rounds)																		
43		Meeting with KDOT and KTA																		
44		One-on-One Stakeholder Meetings																		
45																				
46		3.0 Review Planning Requirements, Existing Plans		ļ																
Project:		ce LRTP Draft Schedu Task	Pro	gress				Summa	ry				Exte	ernal Task	s			De	adline	<u>,</u> 1
Date: T	ue 5/1/07	7 Solit	Mile	estone				Project	Summary	y U			Exte	ernal Miles	stone 📥			_		Ť
		Opin				-														



		May June July August September October Novemb
ID 🟮	Task Name	4/22 4/29 5/6 5/13 5/20 5/27 6/3 6/10 6/17 6/24 7/1 7/8 7/15 7/22 7/29 8/5 8/12 8/19 8/26 9/2 9/9 9/16 9/23 9/30 10/7 10/14 10/21 10/28 11/
47	3.1 Review Transportatoin 2025 Plan	
48	3.2 Review Other Local and Regional Plans	
49	Transportation 2030 Draft Chapters	
50	2006-2009 TIP	
51	South Lawrence Trafficway ROD	
52	KAW Connects Corridor Study	
53	Lawrence/DG County 2006 Future Land Use Plan	
54	Horizon 2020 Comprehesive Land Use Plan	
	Coordinated Public Transportation Development Plan	
55		
56	Johnson County Inter-Campus Transit Op Plan	
57	Local Conservation Plans	
58	Historic Resources, Watershed, Floodplain, Wetlands	
59	MARC Commuter Rail Plan	
60	Regional ITS Architecture Info	
61	Kansas State Transportation Improvement Program	
62	City Corridor Studies	
63	Kansas Statewide LRTP	
64	Lawrence Airport Plan	
	T2030 Committee Minutes	
66	City Water/Sewer CIP	
67	TAZ Population Projections	
68	Summary Report	
69	3.3 Review SAFETEA-LU Planning Requirements	
70		
71	4.0 Evaluate LRTP Goals/ Policies	
72	4.1 Review Current Goals & Objectives	
73	4.2 Identify Additional Goals & Objectives	
74	4.3 Evaluate Consistency with SAFETEA-LU Requirement	
75		
76	5.0 Travel Demand Model	
	5.1 Base Year Model Coordination	
	5.2 Future Year Model Coordination	
78		
79	5.3 Year 2030 Deficiency Analysis	
80	5.4 Roadway Improvement Scenarios	
81		
82	6.0 Identify & Prioritize Transportation Issues	
83	6.1 Develop Initial List of Issues	
84	6.2 Identify Public & Stakeholder Issues	
85	6.3 Analyze Transportation Issues	
86		
87	7.0 Needs Assessment	
88	7.1 Identify Transportation Facilities	
89	7.2 Identify Needs for each Mode	
90	7.3 Identify Potential Improvements	
91		
92	8.0 Financial Forecast and Analysis	
	Task	Progress Summary External Tasks Deadline
Project: Lawre Date: Tue 5/1/0		
	Split	Milestone
		Page 2
		Page 2

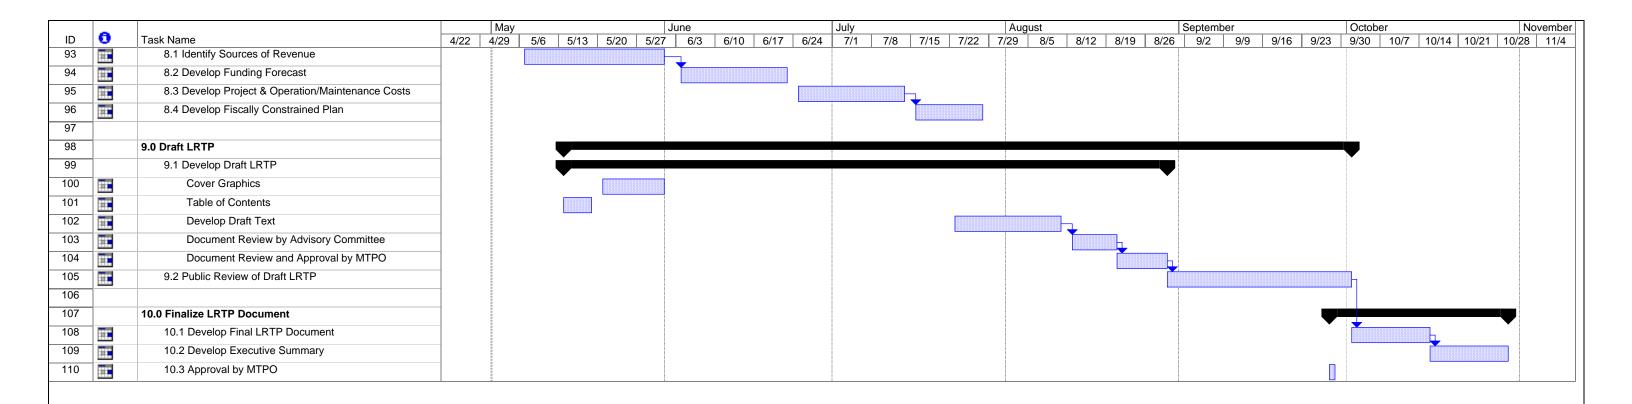

Project: Lawrence LRTP Draft Schedu Date: Tue 5/1/07	Task Split		Progress Milestone	•	Summary Project Summary		External Tasks External Milestone	Deadline	Ł		
		Page 3									
